




**2021 Progress to  
Extended Facilities**

**Cutting out the partition walls  
Now you see me—Now you don't**

**Three 40' containers are  
opened into a workshop  
12m x 7.5m**

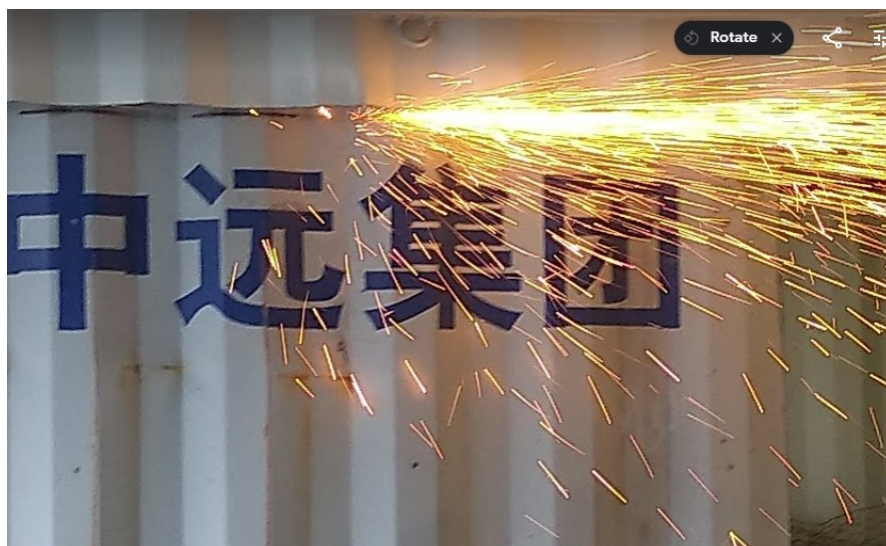

**with our 4th container  
divided into secure store  
and meeting room via  
entrances in photo**

**Construction Acrows  
to be replaced by  
structural posts to  
support the roof**





**Roof Joint preparation for watertight seal prior to internal fit out  
External walls multi layer foil insulated and lined with 12mm ply  
Fitted with work benches - Trial bench weight tested by Les !**



**To gain access for container lorry, field fences needed to be moved  
Fences have been re-erected and post & rail entrance established**

**Power connection has been re-established with care to preserve  
power harvesting from the extensive PV array on the Farm Barn**

